

1. Project Phasing Overview

CONSTRUCTION SCHEDULE & PHASING

PHASE 1 CONSTRUCTION

PHASE 2 CONSTRUCTION



Modular Classrooms/Site Work

Existing Building Abatement/Demolition


Building Addition Academic/Student Life Wing Construction

Existing Building Abatement/Demolition

Music + Performing Arts Wing Construction

2015												2016												2017								
Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept
PHASE 1 CONSTRUCTION																																
												PHASE 2 CONSTRUCTION																				

1. Project Phasing Overview

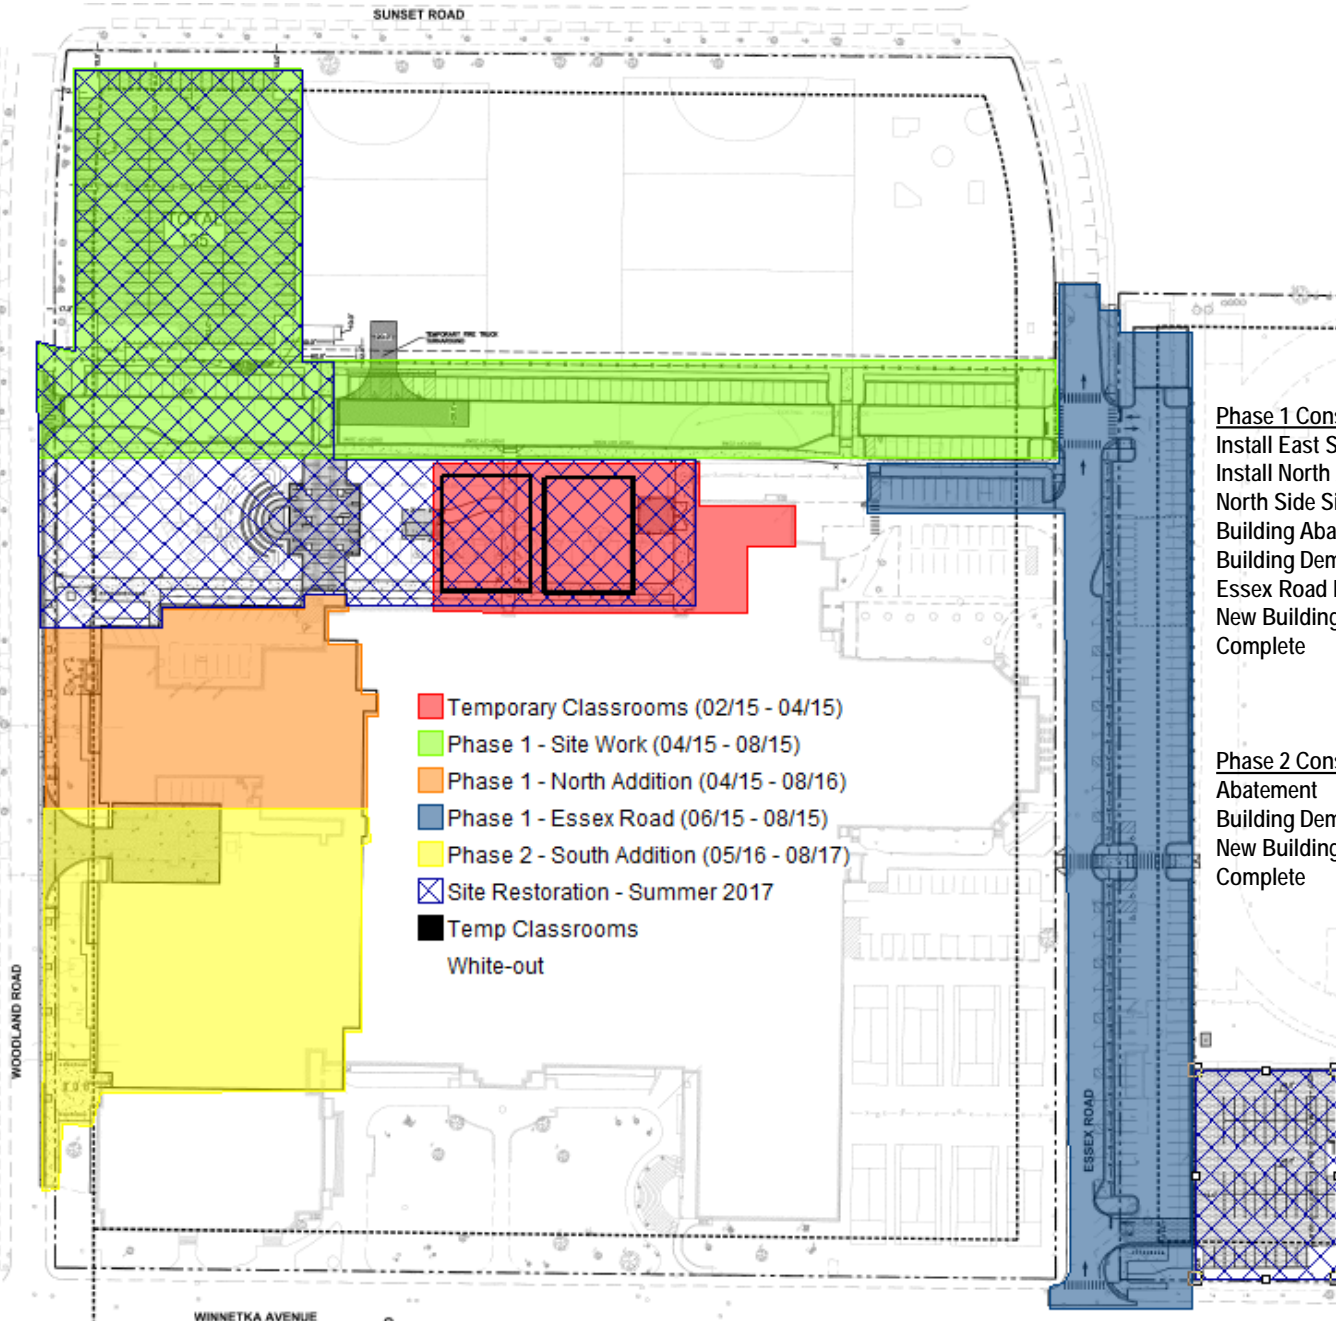

Phase 1 Construction

Install East Side Temporary Parking Lot	December 2014
Install North Annex Modular Classrooms	February 2015- March 2015
North Side Site Work	April 2015 – August 2015
Building Abatement	April 2015 – May 2015
Building Demolition	June 2015 – July 2015
Essex Road Improvements	June 2015 – August 2015
New Building Addition	July 2015 –August 2016
Complete	August 2016 School Year

Phase 2 Construction

Abatement	May 2016 –June 2016
Building Demolition	June 2016 –July 2016
New Building Addition	July 2016 –August 2017
Complete	September 2017 School Year
